Sabre Communications Corporation

Washington Parish Communications Tower
Proposed Construction Schedule
8.30.11

ID	Task Name	Duration	Start	Finish	Predecessors
1					
2	Notice to Proceed	1 day	Fri 8/19/11	Fri 8/19/11	
3	Tower design and Drawings	16 days	Mon 8/22/11	Mon 9/12/11	2
4	Shelter Design and Drawings	42 days	Mon 8/22/11	Tue 10/18/11	2
5	Tower Fabrication	30 days	Tue 9/13/11	Mon 10/24/11	3
6	Shelter Fabrication	42 days	Wed 10/19/11	Thu 12/15/11	4
7	Site Grading and Access	5 days	Mon 10/10/11	Fri 10/14/11	
8	Tower Foundation Installation	5 days	Mon 10/17/11	Fri 10/21/11	7
9	Shelter and Generator Pads	3 days	Mon 10/24/11	Wed 10/26/11	8
10	Erect Tower	10 days	Tue 10/25/11	Mon 11/7/11	5
11	Set Shelter and Generator	3 days	Fri 12/16/11	Tue 12/20/11	6
12	Install Site Grounding	33 days	Tue 11/8/11	Thu 12/22/11	10
13	Final Grade	5 days	Fri 12/23/11	Thu 12/29/11	12
14	Site Fencing	5 days	Fri 12/30/11	Thu 1/5/12	13
15	Completion and Closeout	28 days	Fri 1/6/12	Tue 2/14/12	14

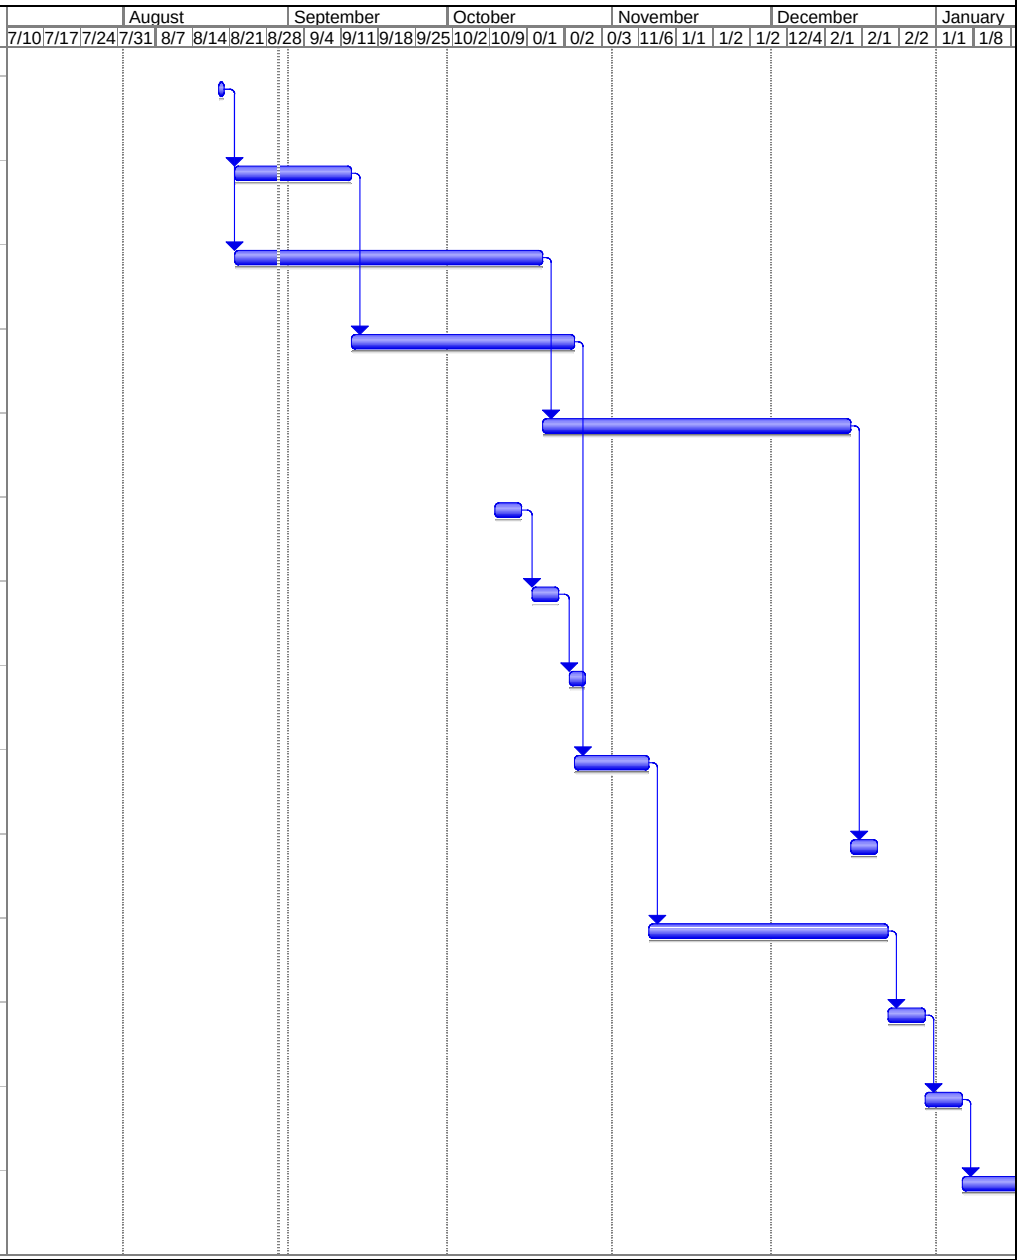

Project: Washington Parish, LA
Date: Tue 8/30/11

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline
